


December 2024 Charter RDOF Projects Installation Status Update:

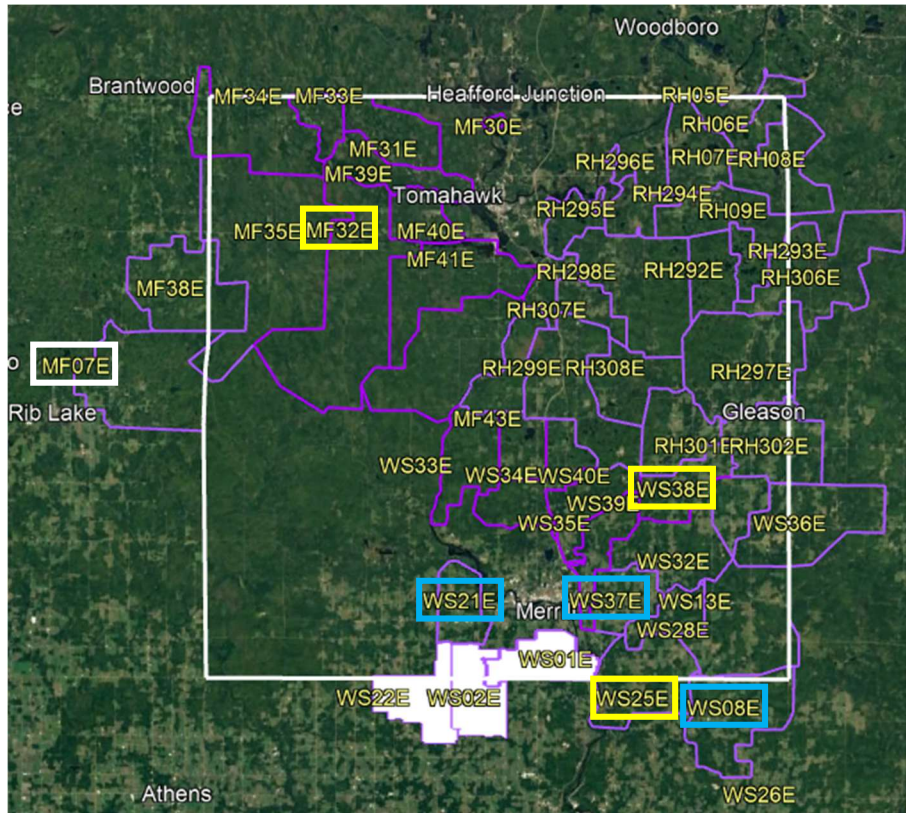

Lincoln County, WI	
OLT	Status
WS22E (WHITE FILL)	Completed
WS02E (WHITE FILL)	Completed
WS01E (WHITE FILL)	Completed
MF07E (WHITE BOX)	Completed
WS21E - under construction pending pole make ready to complete	In Progress -1st-2 nd Quarter 2025
MF32E	In Progress -1st-2 nd Quarter 2025
WS38E	In Progress -1st-2 nd Quarter 2025
WS25E	In Progress -1st-2 nd Quarter 2025
WS08E - currently under construction	In Progress -1st-2 nd Quarter 2025
WS37E - under construction - pending pole make ready to complete	In Progress -1st-2 nd Quarter 2025

For a more detailed, interactive map of the Charter RDOF project, visit the following GIS map link and search for "Lincoln County, WI":

<https://experience.arcgis.com/experience/0b324cabf7b94d9ca34caa9361122d94/>
